

NECP



SCHOOL PROJECT COMMUNITY UPDATE

Tuesday, November 16, 2021 – 6:00 PM

Virtual via ZOOM, Link to register:

https://uso2web.zoom.us/webinar/register/WN_6RjEaq21RRyHwu37o_hqVw

Refer to <https://www.newtonma.gov/government/public-buildings/calendar> for upcoming meeting dates, registration links, and more information!

Construction Activities

- (3) modular classrooms demolished
- Interior abatement, wall demolition, and electrical/plumbing cut and cap has begun
- Demolition of site walkways
- Upcoming
- Continue interior abatement and demolition, including slabs
- Demolish mechanical systems
- Continue site work

Consultant Team

Hill International – Owner’s Project Manager

Arrowstreet – Architect



M. O’Connor Contracting – General Contractor

Contacts

For general project inquiries:

Alex Valcarce – City of Newton Project Manager
(617) 796 - 1600

For project updates, please visit: <https://www.newtonma.gov/government/public-buildings/capital-projects-investing-now-for-newton-s-future/school-projects/necp>

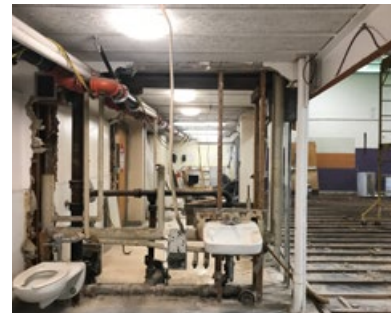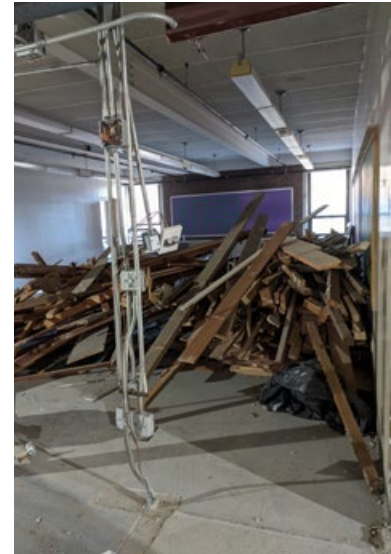

Overall Construction Schedule

Oct. 2021	Ground Breaking
Fall 2022	Substantial Completion
Fall 2022	Occupy School

Save The Dates: NECP Community updates will be the 3rd Tuesday of each month at 6:00PM for the project duration, unless otherwise noted.

December 21, 2021 6:00 PM

January 18, 2022 6:00 PM
