

# NECP



# SCHOOL PROJECT COMMUNITY UPDATE

## July 2022 Update

### Construction Activities

- Finished penetrations through the roof, flashing and metal roof edge
- Progressing work on ramp and sidewalks on site
- Continue framing and MEP at all levels, hang and tape drywall at lower level and level 1
- Installed seismic upgrades to existing CMU
- Installation of exterior storefront and glass
- Exterior priming and painting
- Install metal panels at new entrance

### Upcoming Activities



- Installation of new vestibule storefront and main doors & interior storefront
- Finish interior framing and soffits & MEP rough in, hang and tape drywall at all levels
- Begin interior prime and paint
- Finishing up ramp and sidewalks on site

### Consultant Team

Hill International – Owner’s Project Manager

Arrowstreet – Architect

M. O’Connor Contracting – General Contractor

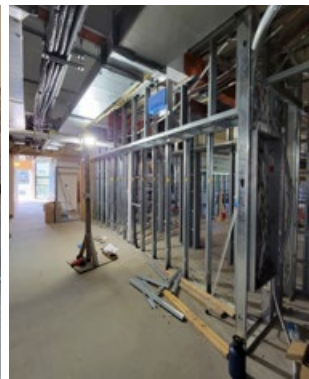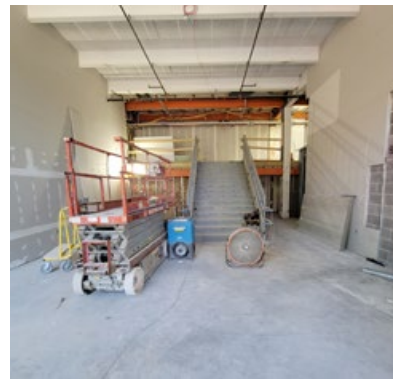

### Contacts

For general project inquiries:

Alex Valcarce – City of Newton Project Manager  
(617) 796 - 1600

### Overall Construction Schedule

Oct. 2021	Ground Breaking
Fall 2022	Substantial Completion
Fall 2022	Occupy School

For project updates, please visit: <https://www.newtonma.gov/government/public-buildings/capital-projects-investing-now-for-newton-s-future/school-projects/necp>
