

NECP



SCHOOL PROJECT COMMUNITY UPDATE

August 2022 Update

Construction Activities

- Continue to work on sidewalks and sloped walks around the site
- Continue framing and MEP at all levels, hang and tape drywall at level 1 & 2
- Continue installation of exterior storefront sealant, glass, and ACM panels at new entry
- Installation of the new elevator rails & cab
- Continue painting at Level 1 & 2
- Started wall tile in restrooms

Upcoming Activities


- Installation of new vestibule storefront and main doors & interior storefront
- Finish hanging & taping drywall & MEP finish devices
- Continue interior prime and paint
- Finishing up sidewalks & preparing for playground equipment

Consultant Team

Hill International – Owner’s Project Manager

Arrowstreet – Architect

M. O’Connor Contracting – General Contractor

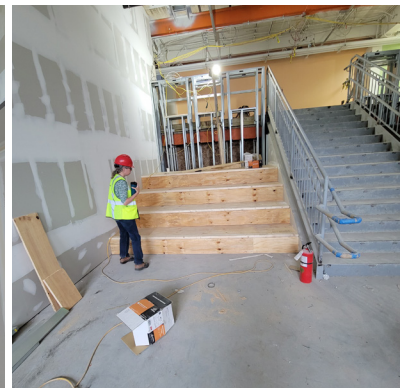

Contacts

For general project inquiries:

Alex Valcarce – City of Newton Project Manager
(617) 796 - 1600

Overall Construction Schedule

Oct. 2021	Ground Breaking
Fall 2022	Substantial Completion
Fall 2022	Occupy School

For project updates, please visit: <https://www.newtonma.gov/government/public-buildings/capital-projects-investing-now-for-newton-s-future/school-projects/necp>
