


# NECP



# SCHOOL PROJECT COMMUNITY UPDATE

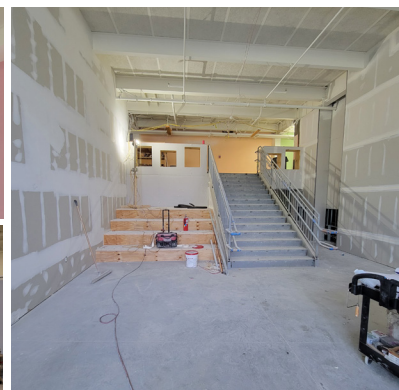

## September 2022 Update

### Construction Activities

- Continue site work including: remaining sidewalks, grading, and prep for playground
- Finished framing and taping, continued painting on all levels
- Continue installation of exterior & interior storefront sealant, glass, and ACM panels
- Began installation of millwork
- Continue electrical, controls, and fire protection installation
- Installed Epoxy flooring in restrooms

### Upcoming Activities

- Installation of new vestibule storefront and main doors
- Install MEP finish devices & HVAC start up
- Continue interior finishes including starting flooring and toilet accessories
- Finishing up sitework including porous plaza, playground, final sidewalks, and plantings

### Consultant Team

Hill International – Owner’s Project Manager

Arrowstreet – Architect

M. O’Connor Contracting – General Contractor

### Contacts

For general project inquiries:

Alex Valcarce – City of Newton Project Manager  
(617) 796 - 1600

### Overall Construction Schedule

Oct. 2021	Ground Breaking
Fall 2022	Substantial Completion
January 2023	NECP Opens

For project updates, please visit: <https://www.newtonma.gov/government/public-buildings/capital-projects-investing-now-for-newton-s-future/school-projects/necp>
